


## Expected Project Construction Schedule

<p><b>Expected Project Start Date:</b> <b><u>May 14th</u></b></p>	
<b>Stage 1</b>	<p><b>Monday May 14, 2018 to Friday, June 22, 2018:</b></p> <p>Construction will begin from the South City Limits to Lindenwood. Traffic will be maintained in both directions, utilizing a single lane closure and flag control.</p> <p>Construction will include road rehabilitation, crushing, shaping, grading, drainage improvements, shoulder work, restoration, and pavement markings.</p> <p>(No roadwork Memorial Day weekend 5/26 to 5/28)</p>
<b>Stage 2</b>	<p><b>Monday June 25, 2018 to Friday, August 31, 2018:</b></p> <p>Road reconstruction will occur from Lindenwood to Hickory, including curb and gutter installation, sidewalk removal and replacements and installation of storm sewer. Water main installation will occur from Lindenwood to the Bridge over the Shiawassee River. Traffic will be maintained in one direction and detour routes will be posted and in effect through mid-August.</p> <p>(No roadwork on Independence Day 7/4)</p>
<b>Stage 3</b>	<p><b>Tuesday, September 4, 2018 to Friday, October 5, 2018:</b></p> <p>Road milling and resurfacing from Hickory to the Bridge over the Shiawassee River will continue, including curb and gutter repair, sidewalk removal and replacement, and installation of storm sewer and water main. Two-way traffic will be maintained utilizing lane closures and flag control.</p> <p>Place the top course of pavement, pavement markings and other miscellaneous work from the southern City limits to the Bridge. Two-way traffic will be maintained utilizing lane closures.</p> <p>(No roadwork on Labor Day 9/4)</p>
<p><b>Expected Project Completion:</b> <b><u>OCTOBER 5<sup>th</sup></u></b></p> <p><small>Dates are predicated upon weather and other conditions and may be subject to change. We will continue to update you with changes to the schedule throughout the summer.</small></p>	

## S Bridge Street Rehabilitation Project From the South City Limits to the Shiawassee River 2018

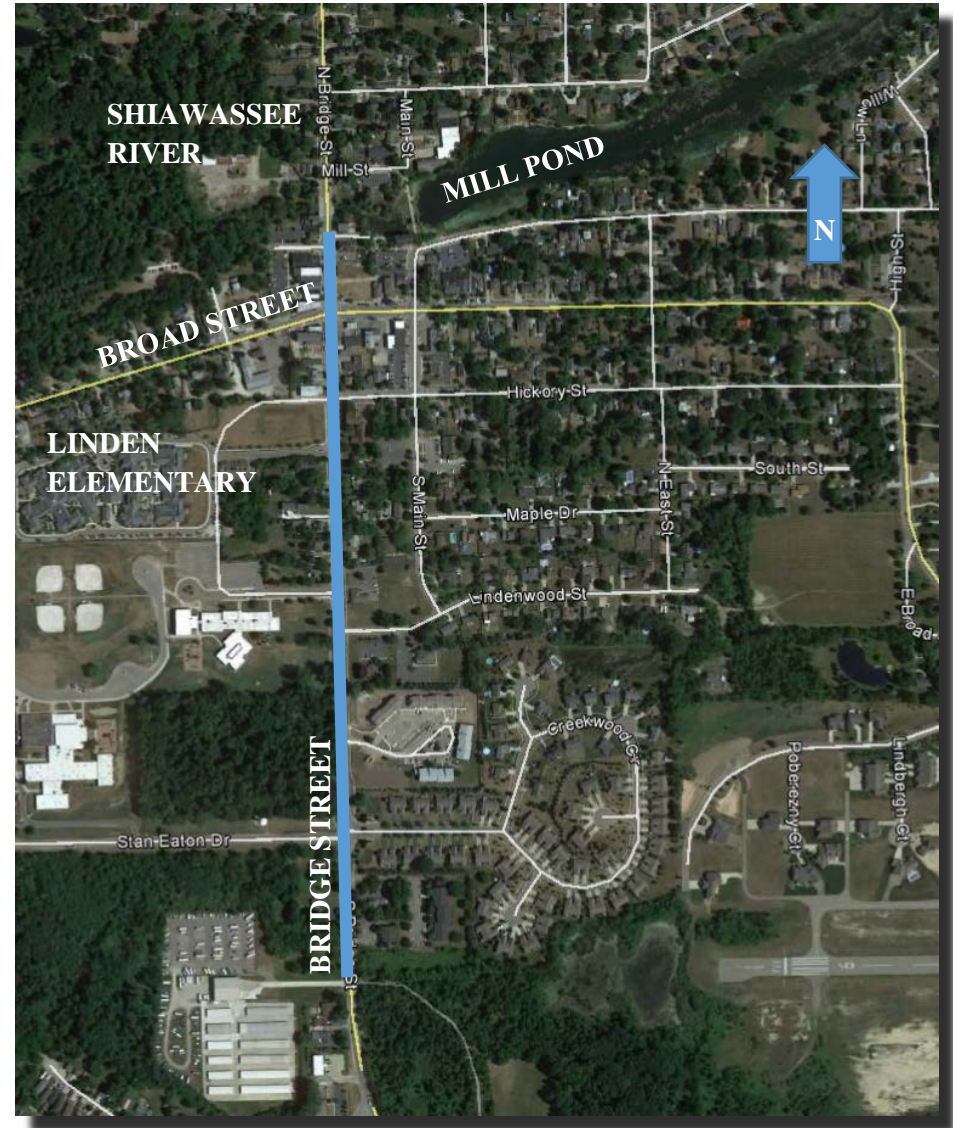

*Utility relocations & tree removal will begin prior to May 2018 and continue throughout the project. Watch for crews working along Bridge Street in the next six months.*

## Bridge Street Rehabilitation Project

The Bridge Street rehabilitation project limits extend from the south City Limits to the south side of the bridge over the Shawasssee River. All side street approaches within these limits will be included in the rehabilitation. The estimated construction cost is \$1.2 million, with 80% of the costs being paid for with Federal and State funds.

### PROJECT WORK:


- ▶ 0.57 miles of road reconstruction/ rehabilitation
- ▶ New curb and gutter installation & replacement
- ▶ Addition of bike lane from the south City Limits to Broad Street
- ▶ New water main and hydrants from Lindenwood to the Bridge
- ▶ Storm sewer replacement and repair (locations vary)
- ▶ Addition of storm sewer for drainage improvements
- ▶ New concrete driveway approaches (locations vary)
- ▶ Sidewalk ramp replacement to meet current standards
- ▶ Driveway culvert replacement (locations vary)
- ▶ New updated signage and pavement markings

### KEY NOTES:

- ▶ Access to all businesses will be maintained throughout the project

## DETOUR ROUTE

### ACCESS TO ALL BUSINESSES WILL BE MAINTAINED THROUGHOUT THE PROJECT

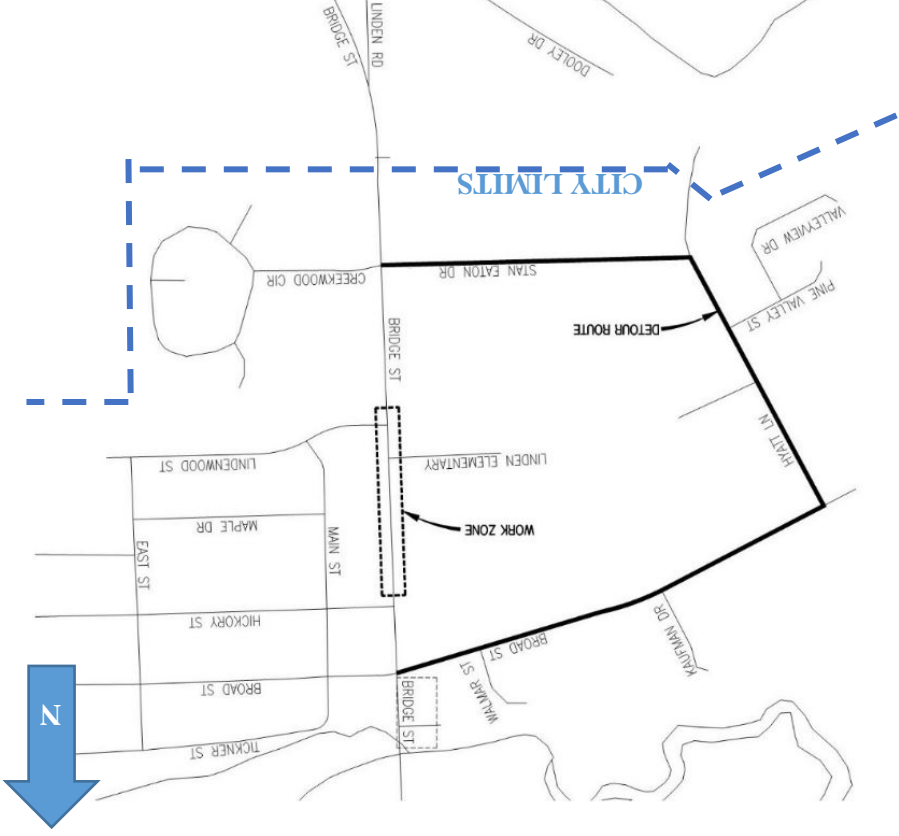

### Northbound or Southbound Bridge Street Detour

One direction will be closed from Lindenwood Street to Hickory Street late June 2018 to Mid-August 2018

- ▶ One lane of traffic (northbound or southbound ) will be detoured using Stan Eaton Drive, Hyatt Lane, and West Broad Street.

- ▶ Traffic in the opposite direction will be maintained during construction, but may be shifted.
